PROTECTED25 / ONE PLACEMENT ATTEMPT

192 footprints; no routing. Local base relief is a proposal, not approved tooling or protection performance.

Teal:13 added controls / orange:fuse / gray:unchanged courtyards. Exact references and pads:actual-board SVGs.

TOP - courtyard allocation view

Plan scales X10 / Y6 points per mm

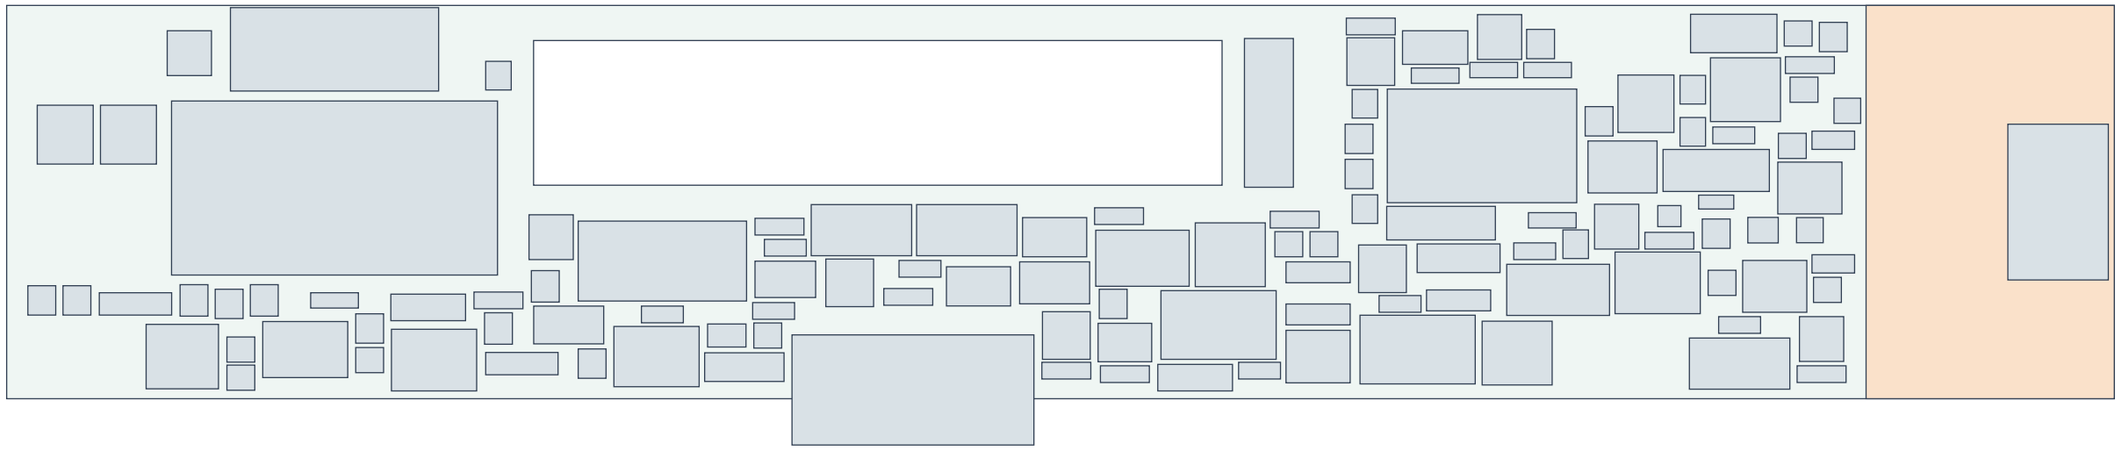

PCB main: X4..94, Y23..51, Z10..11; USB tongue retained. Internal aperture29.4 x10.3, R0.5.

BOTTOM (viewed through board; same X/Y datum) - courtyard allocation view

Plan scales X10 / Y6 points per mm

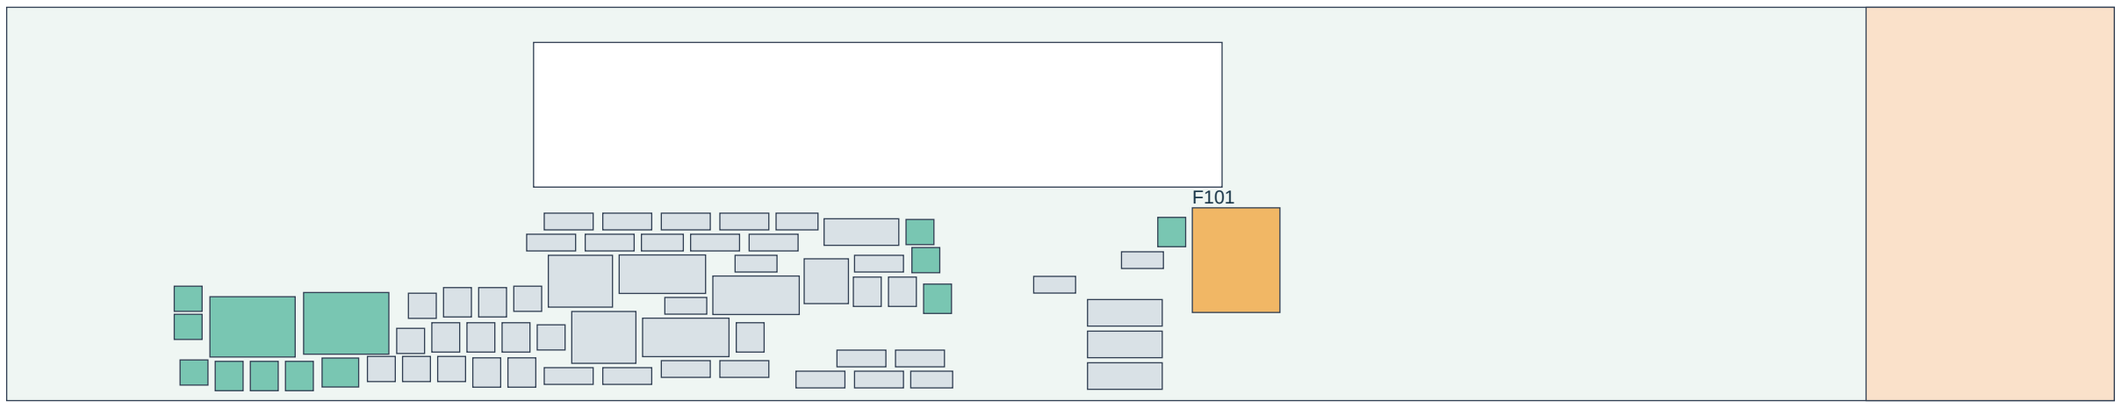

PCB main: X4..94, Y23..51, Z10..11; USB tongue retained. Internal aperture29.4 x10.3, R0.5.

FUSE SECTION AT X56.5 - scale X20 / Z35 drawing points per mm

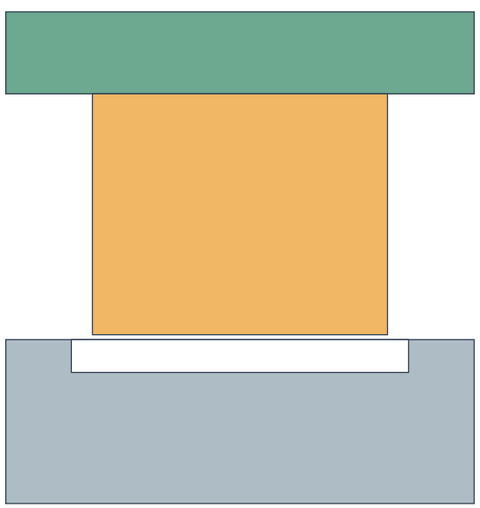

F101 max body6.30 x2.94 x2.94; bottom Z7.06.

Original base Z7: gap0.06; NOT sufficient allocated margin.

Proposed relief: X54.6..58.4 / Y37.4..44.6 / floor Z6.6.

Vertical gap0.46; shortest3D gap0.434; .20 down clears.

Remaining floor1.60; strength/creep/process approval OPEN.

Cell tab to fuse: no route yet; unfused conductor must be restrained/insulated and protection placement approved.

No fuse clearing, turnoff maximum or healthy10s acceptance.
